

# South Deerfield Wastewater Treatment Facility Phase 1 Upgrades Project



**Weekly Project Update (Issued on June 17, 2022)**  
**Town of Deerfield, MA**

## WORK PERFORMED DURING THE WEEK OF JUNE 13, 2022

- Contractor began installation of rebar mat for the proposed Secondary Clarifier.
- Contractor continued repair work to the existing Aeration Basin.
- Contractor began forming electrical pads for the Process Building and installed the electrical cabinets for the Headworks Building.
- Contractor installed safety bollards for the new electrical transformer pad.
- Contractor continued siding construction for the Headworks Building.

## KEY WORK ELEMENTS

- Aeration Basin Repairs
- Secondary Clarifier Rebar Mat Construction
- Headworks Building Siding Construction

## CONTACT INFORMATION

Justin Skelly, P.E.  
Senior Project Manager  
413-567-6310 (x703)  
[justin.skelly@dpcengineering.com](mailto:justin.skelly@dpcengineering.com)

## WORK ANTICIPATED DURING THE WEEK OF JUNE 20, 2022

- Contractor plans to install truss plates, trusses, and monorail for the Process Building.
- Contractor plans to continue rebar installation for the the proposed Secondary Clarifier.
- Contractor plans to begin installation of metal walls and roofs for the Headworks Building.



*Aeration Basin Repairs*




*Clarifier Rebar Mat Construction*



*Transformer Pad Safety Bollards*



*Process Building Electrical Room*

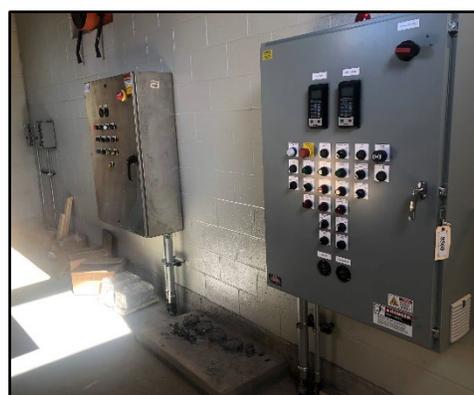

*Headworks Building Electrical Room*



*Headworks Building Siding*
