

South Deerfield Wastewater Treatment Facility Phase 1 Upgrades Project

*Weekly Project Update (Issued on May 13, 2022)
Town of Deerfield, MA*



KEY WORK ELEMENTS

- Process Building Floor Construction
- Secondary Clarifier Sump Construction
- Aeration Basin Dividing Wall Construction

CONTACT INFORMATION


Justin Skelly, P.E.
Senior Project Manager
413-567-6310 (x703)
justin.skelly@dpcengineering.com

WORK PERFORMED DURING THE WEEK OF MAY 9, 2022


- Contractor continued setting forms and rebar for Process Building floor, and continued installing associated site piping.
- Contractor installed rebar and forms for proposed Secondary Clarifier sump walls.
- Contractor began installing forms and rebar for proposed dividing wall on South side of Aeration Basin.

WORK ANTICIPATED DURING THE WEEK OF MAY 16, 2022


- Contractor plans to continue forming Process Building floor.
- Contractor plans to continue installing forms and rebar for proposed dividing wall on South side of Aeration Basin.
- Contractor plans to pour concrete to form proposed Secondary Clarifier sump walls.

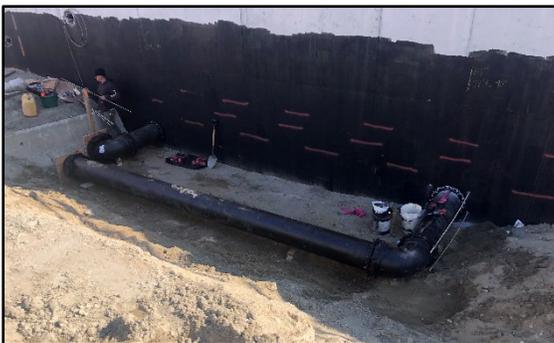

Process Building Site Piping

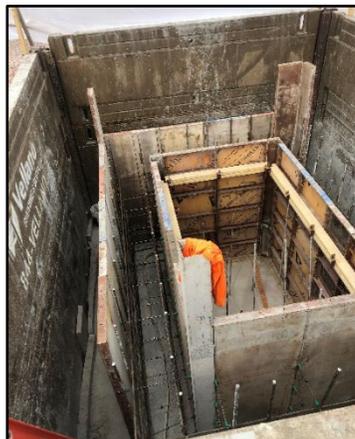

*Secondary Clarifier Sump Construction
and Associated Piping*

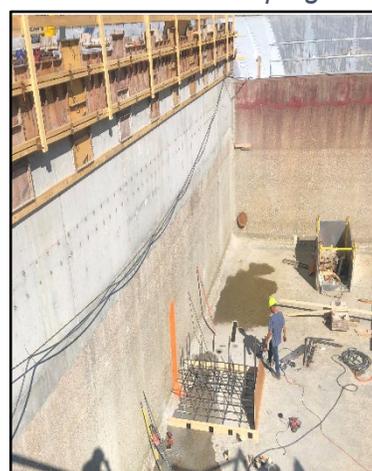

*Aeration Basin Dividing Wall
Construction*



Process Building Floor Construction
