

South Deerfield Wastewater Treatment Facility Phase 1 Upgrades Project



**Weekly Project Update (Issued on May 20, 2022)
Town of Deerfield, MA**

KEY WORK ELEMENTS

- Process Building Floor Construction
- Site Piping and PCB #3
- Aeration Basin Dividing Wall Construction
- Headworks Equipment Install

CONTACT INFORMATION

Justin Skelly, P.E.
Senior Project Manager
413-567-6310 (x703)
justin.skelly@dpcengineering.com

WORK PERFORMED DURING THE WEEK OF MAY 16, 2022

- Contractor poured the Process Building floor, continued installing site piping and installed proposed catch basin (PCB) #3.
- Contractor poured concrete for the proposed Secondary Clarifier sump walls and began shoring to install site piping.
- Contractor began installing the mechanical bar screen and grit dewatering unit in the Headworks Building.

WORK ANTICIPATED DURING THE WEEK OF MAY 23, 2022

- Contractor plans to begin masonry walls for the Process Building and continue associated site piping and backfilling.
- Contractor plans to install proposed Secondary Clarifier site piping and begin building the clarifier slab base.
- Contractor plans to begin installing wall panels for the Headworks Building and continue installing equipment.




Process Building Floor Construction



Headworks Equipment Installation



Process Building Site Piping and PCB #3 Installation

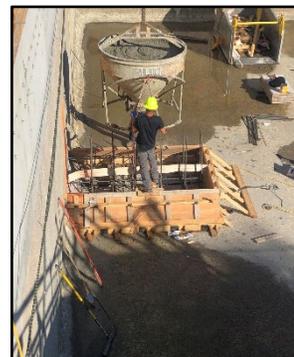

Aeration Basin Dividing Wall Construction
