

# South Deerfield Wastewater Treatment Facility Phase 1 Upgrades Project

*Weekly Project Update (Issued on April 15, 2022)  
Town of Deerfield, MA*



## KEY WORK ELEMENTS

- Process Building Site Piping
- Aeration Basin Cleaning
- Process Building UV Slab
- Distribution Box Demolition

## CONTACT INFORMATION

Justin Skelly, P.E.  
Senior Project Manager  
413-567-6310 (x703)  
[justin.skelly@dpcengineering.com](mailto:justin.skelly@dpcengineering.com)

## WORK PERFORMED DURING THE WEEK OF APRIL 11, 2022

- Contractor began cleaning Aeration Basin No.1 in preparation for concrete repairs to existing walls.
- Contractor continued installing pipe connections to the Process Building in preparation to backfill.
- Contractor poured concrete to form UV Slab in Process Building.
- Contractor demolished existing Distribution Box.

## WORK ANTICIPATED DURING THE WEEK OF APRIL 18, 2022

- Contractor plans to begin backfilling the Process Building and finish installing site pipe connections.
- Contractor plans to continue cleaning Aeration Basin No.1.



*Distribution Box (Existing)*




*Distribution Box (Demolished)*



*Site Piping Installation*



*UV Slab Construction*

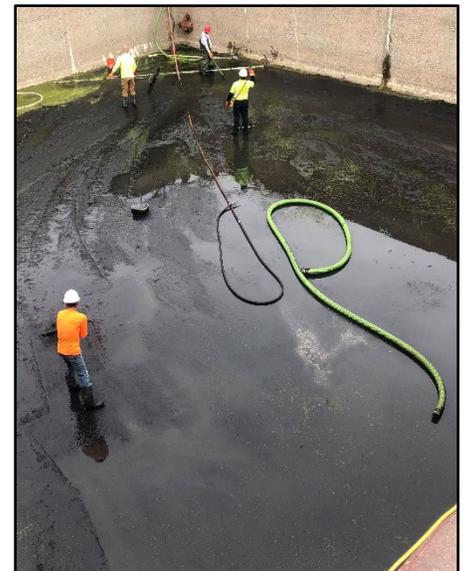

*Aeration Basin No.1 Cleaning*
