

South Deerfield Wastewater Treatment Facility Phase 1 Upgrades Project

*Weekly Project Update (Issued on January 28, 2022)
Town of Deerfield, MA*



KEY WORK ELEMENTS

- Headworks Building Pads
- Process Building Wall Construction

CONTACT INFORMATION

Justin Skelly, P.E.
Senior Project Manager
413-567-6310 (x703)
justin.skelly@dpcengineering.com

WORK PERFORMED DURING THE WEEK OF JANUARY 24, 2022

- Contractor continued form installation for the Process Building foundation walls and prepared for concrete pour next week.
- Contractor constructed forms for the Headworks Building grit dewatering unit mounting pad and exterior entrance pads.

WORK ANTICIPATED DURING THE WEEK OF JANUARY 31, 2022


- Contractor plans to pour concrete pads for Headworks Building entrances and for grit dewatering unit.
- Contractor plans to pour concrete for the north foundation wall of the Process Building, and continue installing rebar and forms for remaining foundation walls.
- Contractor plans to apply base coat of paint for Headworks Building CMU Walls.



Process Building Wall Construction (Looking Northwest)



Headworks Building Grit Dewatering Mounting Pad Forms

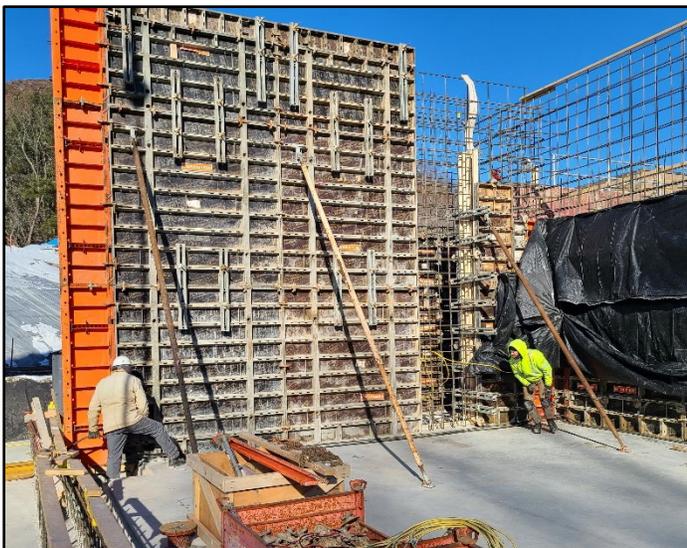

Process Building Wall Construction (Looking West)



Headworks Building Exterior Concrete Pad
