

# South Deerfield Wastewater Treatment Facility Phase 1 Upgrades Project

*Weekly Project Update (Issued on December 3, 2021)  
Town of Deerfield, MA*



## KEY WORK ELEMENTS

- Headworks Building Roof and Electrical Work
- Process Building Slab Construction

## CONTACT INFORMATION


Justin Skelly, P.E.  
Senior Project Manager  
413-567-6310 (x703)  
[justin.skelly@dpcengineering.com](mailto:justin.skelly@dpcengineering.com)

## WORK PERFORMED DURING THE WEEK OF NOVEMBER 29, 2021

- Contractor completed installation of ice/water shield on Headworks Building roof.
- Contractor began rough electrical work inside the Headworks Building.
- Contractor set proposed Sewer Manhole #1.
- Contractor poured concrete for half of the Process Building slab.

## WORK ANTICIPATED DURING THE WEEK OF DECEMBER 6, 2021

- Contractor plans to strip forms, finish sump area rebar work and pour remaining slab for the Process Building foundation.
- Contractor plans to continue rough electrical work inside the Headworks Building.
- Contractor plans to complete Headworks Building drain and form exterior pads.

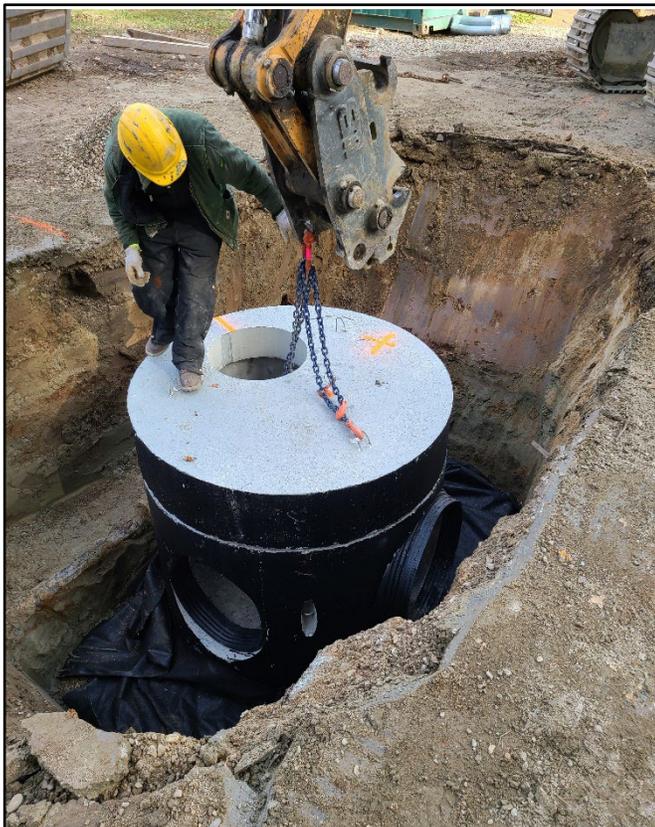

*Sewer Manhole #1*



*Headworks Building (Looking West)*



*Process Building Slab Pour*
