

South Deerfield Wastewater Treatment Facility Phase 1 Upgrades Project



**Weekly Project Update (Issued on November 19, 2021)
Town of Deerfield, MA**

KEY WORK ELEMENTS

- Headworks Building Construction
- Process Building Excavation and Slab Preparation

CONTACT INFORMATION

Justin Skelly, P.E.
Senior Project Manager
413-567-6310 (x703)
justin.skelly@dpcengineering.com

WORK PERFORMED DURING THE WEEK OF NOVEMBER 15, 2021

- Contractor installed top plates, roof trusses and roof sheathing for the Headworks Building.
- Contractor installed 6" DI scum pipe to connect the Aeration Basin to the Proposed Process Building.
- Contractor completed prep work for the Proposed Process Building slab.

WORK ANTICIPATED DURING THE WEEK OF NOVEMBER 22, 2021


- Contractor to continue construction on Headworks Building roof.
- Contractor to begin laying out forms and rebar for the proposed Process Building foundation.



Installation of 6" DI Scum Pipe



Headworks Building (Looking Southwest)

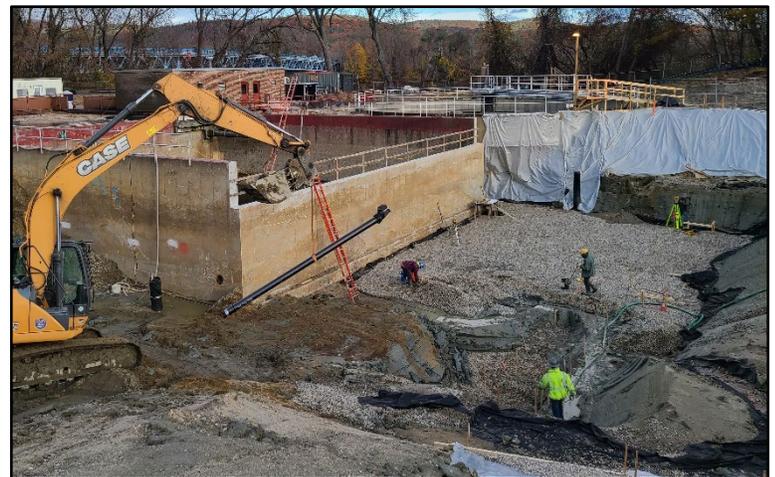

Process Building Slab Preparation
