

South Deerfield Wastewater Treatment Facility Phase 1 Upgrades Project

*Weekly Project Update (Issued on July 15, 2022)
Town of Deerfield, MA*



WORK PERFORMED DURING THE WEEK OF JULY 11, 2022

- Contractor began installing roof trusses for the Process Building.
- Contractor began alternating concrete pours for the proposed Secondary Clarifier slab.
- Contractor completed siding and roof construction and began installing doors and windows for the Headworks Building.
- Contractor began piping installation in the basement of the Process Building.
- Contractor finished installing staging in the Aeration Basin for upcoming concrete work in the North side of the Process Building.

KEY WORK ELEMENTS

- Headworks Building Roof, Doors, and Windows Installation
- Secondary Clarifier Slab Construction
- Process Building Roof Trusses Installation

CONTACT INFORMATION

Justin Skelly, P.E.
Senior Project Manager
413-567-6310 (x703)
justin.skelly@dpcengineering.com

WORK ANTICIPATED DURING THE WEEK OF JULY 18, 2022


- Contractor plans to finish pouring the proposed Secondary Clarifier slab.
- Contractor plans to continue truss and plywood installation for the Process Building roof.
- Contractor plans to continue mechanical piping and electrical installation in the basement of the Process Building.




Aeration Basin Stages



Secondary Clarifier Slab Construction

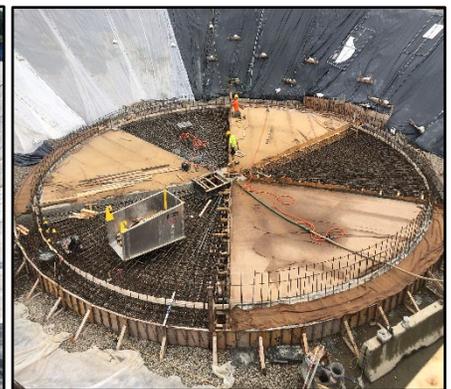

*Process Building Roof Trusses Installation
(Looking West)*

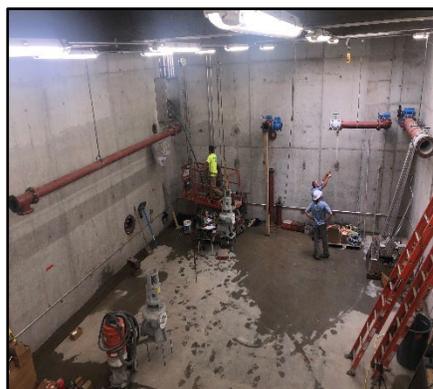

*Process Building Basement
Mechanical Piping*



*Headworks Building Doors
and Windows installation*
