

# South Deerfield Wastewater Treatment Facility Phase 1 Upgrades Project

*Weekly Project Update (Issued on July 22, 2022)  
Town of Deerfield, MA*



## WORK PERFORMED DURING THE WEEK OF JULY 18, 2022

- Contractor continued installation of roof trusses for the Process Building.
- Contractor continued mechanical and electrical piping installation in the basement of the Process Building.
- Contractor completed concrete pours for the proposed Secondary Clarifier slab.
- Contractor finished installing doors and windows for the Headworks Building.
- Contractor began construction of the proposed Effluent Flow Distribution Channel in Aeration Basin No.1.

## KEY WORK ELEMENTS

- Secondary Clarifier Slab Construction
- Process Building Roof Trusses Installation
- Aeration Basin No.1 Effluent Distribution Channel Construction

## CONTACT INFORMATION


Justin Skelly, P.E.  
Senior Project Manager  
413-567-6310 (x703)  
[justin.skelly@dpcengineering.com](mailto:justin.skelly@dpcengineering.com)

## WORK ANTICIPATED DURING THE WEEK OF JULY 25, 2022

- Contractor plans to begin wall construction for the proposed Secondary Clarifier.
- Contractor plans to begin sealant application for the Headworks Building.
- Contractor plans to finish installing trusses and begin roof construction for the Process Building.



*Secondary Clarifier Slab Construction*

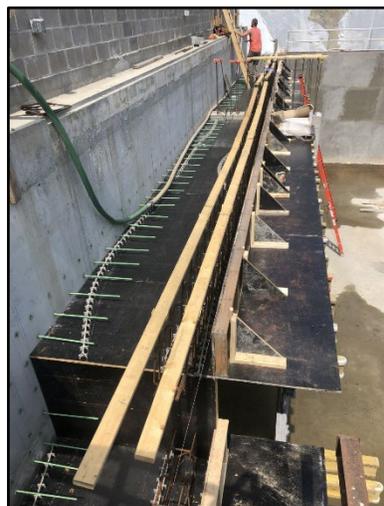

*Aeration Basin Effluent Distribution Channel Construction*



*Headworks Building Doors and Windows installation*



*Process Building Roof Trusses Installation*



*Process Building Basement Piping*
