

# South Deerfield Wastewater Treatment Facility Phase 1 Upgrades Project



**Weekly Project Update (Issued on November 10, 2022)  
Town of Deerfield, MA**

## WORK PERFORMED DURING THE WEEK OF NOVEMBER 7, 2022

- Contractor continued installation of metal siding and roofing on the Process Building, including the installation of snow stops, gutters, and down spouts.
- Contractor completed concrete pour for Aeration Basin No. 1 East and West wall additional elevation.
- Contractor began forming launder wall sections at the Secondary Clarifier.
- Contractor began installation of 14-inch ductile iron sewer pipe between the Secondary Clarifier and Aeration Basin No. 1 tie-in.

## KEY WORK ELEMENTS

- Metal Siding Installation on Process Building
- Aeration Basin No. 1 East and West Wall Concrete Pour
- 14-inch Ductile Iron Sewer Pipe Installation

## WORK ANTICIPATED DURING THE WEEK OF NOVEMBER 14, 2022


- Contractor plans to continue installation of 14-inch ductile iron sewer tie-ins at Aeration Basin No. 1.
- Contractor plans to continue demolition of the Effluent Tank.
- Contractor plans to install temporary winter paving.
- Contractor plans to continue forming launder wall sections.

## CONTACT INFORMATION

Justin Skelly, P.E.  
Senior Project Manager  
413-567-6310 (x703)  
[justin.skelly@dpcengineering.com](mailto:justin.skelly@dpcengineering.com)



*Process Building North Side Siding*

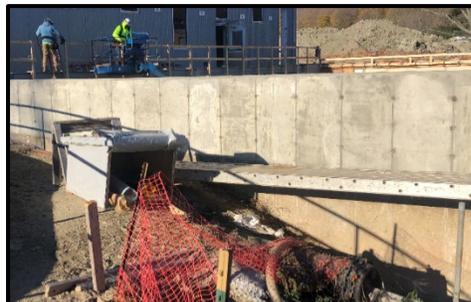


*Aeration Basin East Wall  
Additional Elevation*



*Aeration Basin West Wall  
Additional Elevation*



*Secondary Clarifier Launder Wall  
Footing Forms*

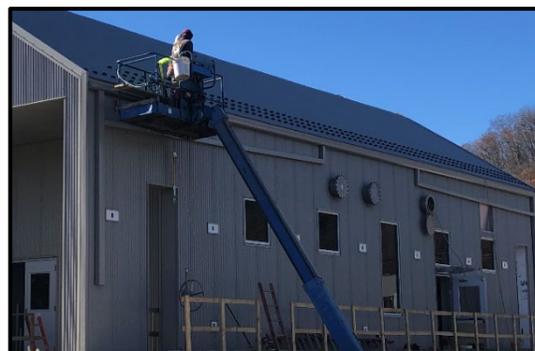

*Process Building Roofing, Snow Stops,  
Gutters, and Down Spouts*



*14-inch Ductile Iron  
Sewer Pipe*
