

South Deerfield Wastewater Treatment Facility Phase 1 Upgrades Project



**Weekly Project Update (Issued on November 23, 2022)
Town of Deerfield, MA**

WORK PERFORMED DURING THE WEEK OF NOVEMBER 21, 2022

- Contractor completed wall forms at the Secondary Clarifier in preparation for Wednesday's concrete pour.
- Contractor completed installation of metal wall panels on the Process Building and began caulking the window joints.
- Contractor completed widening of the site driveway with millings on compacted gravel.
- Contractor continued miscellaneous electrical installations in the Process Building, including conduit, lighting, and panel boards.
- Contractor completed concrete pour for Secondary Clarifier wall section.
- Contractor began excavating around 14-inch drain pipe at Aeration Basin in preparation for next week's tie-in.

KEY WORK ELEMENTS

- Finish Process Building Metal Siding Installation
- Driveway Widening
- Secondary Clarifier Wall Section Pour

CONTACT INFORMATION

Justin Skelly, P.E.
Senior Project Manager
413-567-6310 (x703)
justin.skelly@dpcengineering.com

WORK ANTICIPATED DURING THE WEEK OF NOVEMBER 28, 2022

- Contractor plans to have diver plug line in Aeration Basin No. 2 in order to proceed with the 14-inch drain tie-ins.
- Contractor plans to begin forming next section of Secondary Clarifier wall.
- Contractor plans to finish backfilling Secondary Clarifier.
- Contractor plans to continue miscellaneous electrical installations in the Process Building.
- Contractor plans to begin loading dock foundation.




Secondary Clarifier Wall Forms



Process Building Completed Metal Siding



Driveway Widening

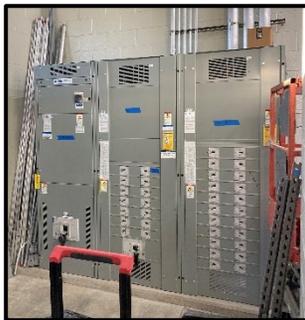

Electrical Installations in Process Building



Secondary Clarifier Wall Concrete Pour



Aeration Basin 14-inch
Pipe Excavation
