

South Deerfield Wastewater Treatment Facility Phase 1 Upgrades Project



**Weekly Project Update (Issued on February 9, 2023)
Town of Deerfield, MA**

WORK PERFORMED DURING THE WEEK OF FEBRUARY 6, 2023

- Contractor continued stripping forms and building forms for Aeration Basin influent structure.
- Contractor continued electrical duct bank installation on the south side of the Process Building, including conduit installation, form work, and rebar installation.
- Contractor completed form installation and concrete pour for Aeration Basin No. 1 center column.
- Contractor continued working on forms for Aeration Basin No. 1 dividing wall footings.
- Contractor completed concrete pour for Aeration Basin influent structure.
- Contractor continued working on installation of Secondary Clarifier control panel.

KEY WORK ELEMENTS

- Electrical Duct Bank Installation
- Aeration Basin Center Column and Influent Structure Concrete Pours
- Aeration Basin Dividing Wall Footing Form Construction

CONTACT INFORMATION

Justin Skelly, P.E.
Senior Project Manager
413-567-6310 (x703)
justin.skelly@dpcengineering.com

WORK ANTICIPATED DURING THE WEEK OF FEBRUARY 13, 2023

- Contractor plans to excavate, form, and tie the generator pad.
- Contractor plans to form and pour Aeration Basin No. 1 dividing wall footings.
- Contractor plans to backfill between the Operations Building and Aeration Basin influent structure.
- Contractor plans to paint process piping.




Stripping/Building Forms for Influent Structure




Electrical Duct Bank



Aeration Basin Center Column Form Installation

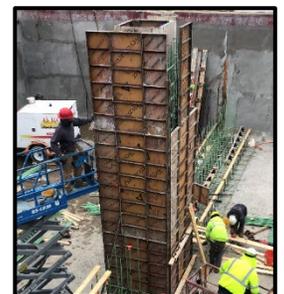

Aeration Basin Center Column Concrete Pour

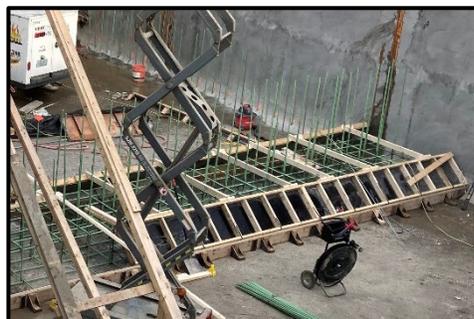

Aeration Basin Dividing Wall Footing Forms



Influent Structure Concrete Pour



Secondary Clarifier Control Panel
