

# South Deerfield Wastewater Treatment Facility Phase 1 Upgrades Project



**Weekly Project Update (Issued on February 16, 2023)  
Town of Deerfield, MA**

## WORK PERFORMED DURING THE WEEK OF FEBRUARY 13, 2023

- Contractor completed switch gear equipment installation in the Headworks Building.
- Contractor continued electrical duct bank installation from Headworks Building to the Process Building.
- Contractor continued forming center wall base and installing rebar in Aeration Basin No. 1.
- Contractor completed painting of piping in the lower level of the Process Building.
- Contractor completed concrete pour of center wall base in Aeration Basin No. 1.
- Contractor began installation of I-beam supports over Process Building UV area.
- Contractor continued backfilling the North side of the Secondary Clarifier.

## KEY WORK ELEMENTS

- Electrical Duct Bank Installation
- Aeration Basin No. 1 Center Wall Forming, Rebar Installation, and Concrete Pour
- Painting of Process Piping

## CONTACT INFORMATION

Justin Skelly, P.E.  
Senior Project Manager  
413-567-6310 (x703)  
[justin.skelly@dpcengineering.com](mailto:justin.skelly@dpcengineering.com)

## WORK ANTICIPATED DURING THE WEEK OF FEBRUARY 20, 2023

- Contractor plans to form and pour generator pad frost walls.
- Contractor plans to form, tie, and pour new wall footings in Aeration Basin No. 1.
- Contractor plans to continue with miscellaneous site cleanup and grading around the Process Building and roadway.




Switch Gear Equipment



Electrical Duct Bank




Aeration Basin Center Wall Forming and Rebar Installation

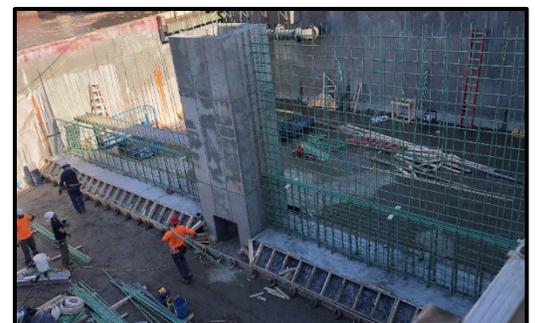

Painted Process Piping



Aeration Basin Center Wall Concrete Pour

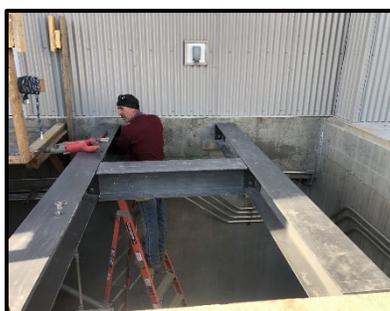

UV I-Beam Supports



Backfilling Secondary Clarifier
