

South Deerfield Wastewater Treatment Facility Phase 1 Upgrades Project



**Weekly Project Update (Issued on March 9, 2023)
Town of Deerfield, MA**

WORK PERFORMED DURING THE WEEK OF MARCH 6, 2023

- Contractor continued pulling cable to Headworks Building and installing cable into Electrical Room switchgear.
- Contractor excavated existing ductile iron pipe and worked on pipe tie-in on the east side of the site, including coring of 22-inch and 28-inch holes into existing concrete wall for future pipe connections.
- Contractor completed concrete pour for Aeration Basin No. 1 center wall section and removed the forms once complete.
- Contractor completed forms for Aeration Basin No. 1 north wall.
- Contractor completed forms for generator pad footings.
- Contractor continued backfilling the Process Building.

KEY WORK ELEMENTS


- Headworks Building Cable Installation
- Aeration Basin No. 1 Center Wall Concrete Pour
- Form Construction for Aeration Basin No. 1 North Wall and Generator Pad Footings

CONTACT INFORMATION

Justin Skelly, P.E.
Senior Project Manager
413-567-6310 (x703)
justin.skelly@dpcengineering.com

WORK ANTICIPATED DURING THE WEEK OF MARCH 13, 2023


- Contractor plans to form and pour Aeration Basin No. 1 north wall (second section).
- Contractor plans to form and pour generator pad frost walls.
- Contractor plans to continue backfilling Process Building.
- Contractor plans to continue wiring switchboards in the Headworks Building.

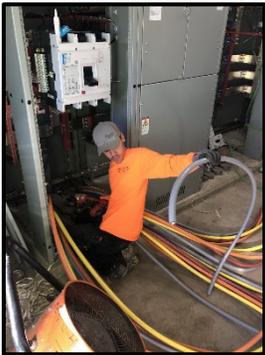

Headworks Electrical

DI Pipe Excavation

Aeration Basin No. 1 Center Wall Concrete Pour

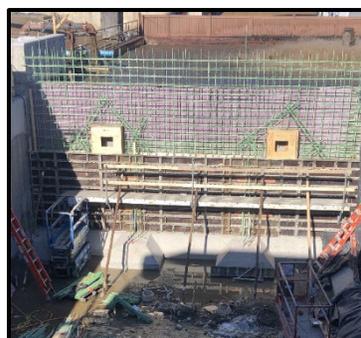

Coring Holes

Aeration Basin North Wall Forms

Generator Pad Footing Forms

Backfilling Process Building
