

South Deerfield Wastewater Treatment Facility Phase 1 Upgrades Project



**Weekly Project Update (Issued on March 16, 2023)
Town of Deerfield, MA**

WORK PERFORMED DURING THE WEEK OF MARCH 13, 2023

- Contractor completed form removal for generator pad and completed concrete pour for walls.
- Contractor completed form removal for Aeration Basin No. 1 center wall.
- Contractor began wiring the control cabinets in the Process Building.
- Contractor diverted water runoff from work area on east side of concrete wall at core penetrations.
- Contractor continued backfilling the south side of the Process Building.

KEY WORK ELEMENTS


- Generator Pad Wall Concrete Pour
- Control Cabinet Wiring in the Process Building
- Backfilling Process Building

CONTACT INFORMATION


Justin Skelly, P.E.
Senior Project Manager
413-567-6310 (x703)
justin.skelly@dpcengineering.com

WORK ANTICIPATED DURING THE WEEK OF MARCH 20, 2023

- Contractor plans to form and pour Aeration Basin No. 1 final wall section.
- Contractor plans to form and pour generator pad slab.
- Contractor plans to backfill generator pad.
- Contractor plans to set transformer and generator.

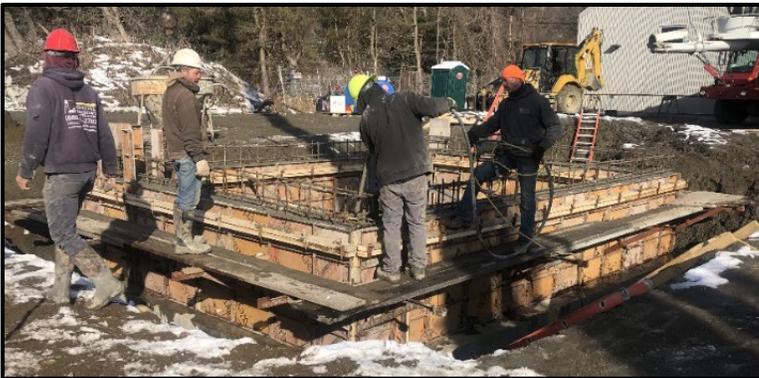

Generator Pad Wall Concrete Pour

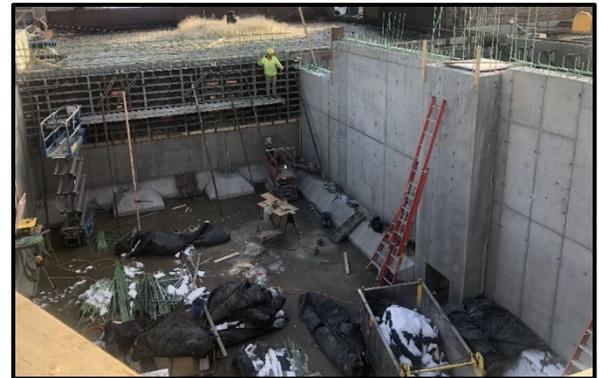

Aeration Basin No. 1 Center Wall After Form Removal



Control Cabinet Wiring



Backfilling South Side of Process Building
