

South Deerfield Wastewater Treatment Facility Phase 1 Upgrades Project



**Weekly Project Update (Issued on March 23, 2023)
Town of Deerfield, MA**

WORK PERFORMED DURING THE WEEK OF MARCH 20, 2023

- Contractor completed form removal from Aeration Basin No. 1 north wall pour.
- Contractor began backfilling and compacting the generator pad.
- Contractor set PVC conduit into place at the generator pad.
- Contractor completed forms and concrete pour for generator pad floor and bollards.
- Contractor continued conduit installation and wiring in the Process Building and Headworks Building.
- Contractor completed 24-inch return tie-in at Aeration Basin No. 1.

KEY WORK ELEMENTS

- Aeration Basin No. 1 Form Removal
- Generator Pad Floor Concrete Pour
- 24-inch tie-in at Aeration Basin No. 1

CONTACT INFORMATION

Justin Skelly, P.E.
Senior Project Manager
413-567-6310 (x703)
justin.skelly@dpcengineering.com

WORK ANTICIPATED DURING THE WEEK OF MARCH 27, 2023

- Contractor plans to form and pour Aeration Basin No. 1 channel support walls.
- Contractor plans to pull wire to generator pad.
- Contractor plans to set generator and stairs.
- Contractor plans to continue with miscellaneous grading throughout the site.




Aeration Basin No. 1 Form Removal



Backfilled Generator Pad
with PVC Conduit



Generator Pad Floor Forms

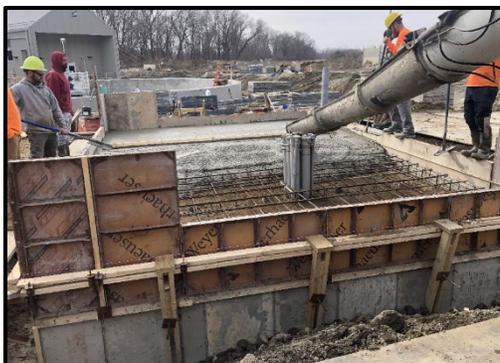

Generator Pad Floor Concrete Pour



Miscellaneous Wiring



Aeration Basin 24-inch Tie-In
