

# South Deerfield Wastewater Treatment Facility Phase 1 Upgrades Project



**Weekly Project Update (Issued on April 14, 2023)**  
**Town of Deerfield, MA**

## WORK PERFORMED DURING THE WEEK OF APRIL 10, 2023

- Contractor continued forming Aeration Channel wall and North wall for Basin No. 1 concrete pour.
- Contractor began installation of handrails in the Process Building.
- Contractor continued farmland restoration and site grading.
- Contractor completed concrete pour at Aeration Basin No. 1 wall.
- Contractor completed installation of bollards in front of Transformer Pad.
- Contractor completed connecting scum line into Aeration Tank and associated backfilling.
- Contractor began wiring in controls at new generator.

## KEY WORK ELEMENTS

- Aeration Basin Wall Concrete Pour
- Farmland Restoration and Site Grading
- Transformer Pad Bollards Installation

## CONTACT INFORMATION

Justin Skelly, P.E.  
Senior Project Manager  
413-567-6310 (x703)  
[justin.skelly@dpcengineering.com](mailto:justin.skelly@dpcengineering.com)

## WORK ANTICIPATED DURING THE WEEK OF APRIL 17, 2023

- Contractor plans to form and tie remaining Aeration Basin No. 1 wall extension.
- Contractor plans to continue handrail installation in the Process Building.
- Contractor plans to begin installation of Aerator Panel conduit.
- Contractor plans to continue site grading around the Secondary Clarifier and Loading Dock.



Forming Aeration Channel Wall



Process Building Handrails




Site Grading/Farmland Restoration



Aeration Channel Wall  
Concrete Pour



Bollard Installation/Concrete Pour

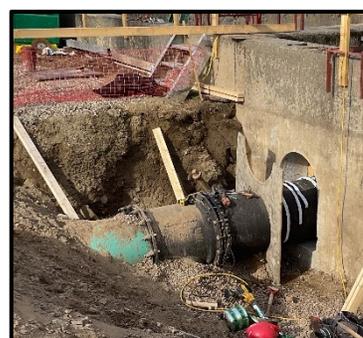

Aeration Tank Scum  
Line Connection



Generator Wiring
