

South Deerfield Wastewater Treatment Facility Phase 1 Upgrades Project



Weekly Project Update (Issued on July 28, 2023)
Town of Deerfield, MA

WORK PERFORMED DURING THE WEEK OF JULY 24, 2023

- Contractor continued installation of Operations Building roof.
- Contractor completed extraction of grit and debris using the Vacuum Truck and began pressure washing walls in the Aeration Basin North Tank.
- Contractor continued installation of conduits and wiring for aerators and mixers in the Aeration Tank.
- Contractor completed connection of the new WAS line to the Waste Sludge Pumping Building.
- Contractor completed startup of the Grit King equipment.
- Contractor began demolition of the Aeration Basin North Tank Channel.
- Contractor began extension of plant water line to the Aeration Basin North Tank.
- Contractor completed generator and Grit King O&M training with the WWTF crew.

KEY WORK ELEMENTS


- Aeration Basin North Tank Cleaning
- Waste Sludge Pumping Building WAS Line Connection
- Aeration Basin North Tank Channel Demolition

CONTACT INFORMATION

Justin Skelly, P.E.
Senior Project Manager
413-567-6310 (x703)
justin.skelly@dpcengineering.com

WORK ANTICIPATED DURING THE WEEK OF JULY 31, 2023

- Contractor plans to drill and install rebar for the Aeration Basin North Tank wall extension.
- Contractor plans to continue plant water line extension.
- Contractor plans to continue installation of Operations Building roof.

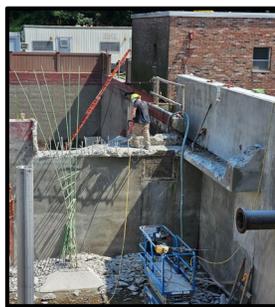

Aeration Basin Channel Demolition

WAS Line Connection



Aeration Basin Cleaning

Aerators Conduit and Wiring
