

South Deerfield Wastewater Treatment Facility Phase 1 Upgrades Project



**Weekly Project Update (Issued on August 17, 2023)
Town of Deerfield, MA**

WORK PERFORMED DURING THE WEEK OF AUGUST 14, 2023

- Contractor completed removal of forms for Aeration Basin North Tank center column.
- Contractor completed removal of forms for Aeration Basin North Tank wall extension on north side.
- Contractor completed filling in form pin holes on the North Tank extension walls.
- Contractor started excavating around the outside of the old Secondary Clarifier for wall extensions.
- Contractor completed coring a 36-inch hole into the center wall of the Aeration Basin North Tank.
- Contractor looked into the issue with RAS Pump No. 1 shutting down, and the pump was operating properly.

KEY WORK ELEMENTS

- North Tank Center Column and Wall Extension Form Removal
- Excavating Around Old Secondary Clarifier
- Coring 36-inch Hole into North Tank Center Wall

CONTACT INFORMATION

Justin Skelly, P.E.
Senior Project Manager
413-567-6310 (x703)
justin.skelly@dpcengineering.com

WORK ANTICIPATED DURING THE WEEK OF AUGUST 21, 2023

- Contractor plans to tie rebar for Aeration Basin dividing wall.
- Contractor plans to continue aerator panel wiring.
- Contractor plans to continue miscellaneous site grading.
- Contractor plans to install Grit Tank grating beams.
- Contractor plans to pour Aeration Basin wall footings.




*North Tank Center Column
Form Removal*



*North Tank Wall Extension
Form Removal*



*Filling in Wall Extension
Pin Holes*

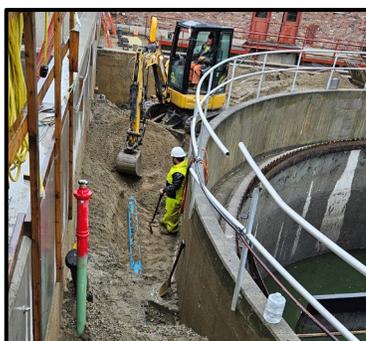

Secondary Clarifier Excavation



North Tank Center Wall Coring
