

South Deerfield Wastewater Treatment Facility Phase 1 Upgrades Project



**Weekly Project Update (Issued on August 24, 2023)
Town of Deerfield, MA**

WORK PERFORMED DURING THE WEEK OF AUGUST 21, 2023

- Contractor completed concrete pour for center wall in North Aeration Tank.
- Contractor started to demolish old clarifier launder walls and demolished 1.5 feet of the North Aeration Tank top wall.
- Contractor completed tie-in of plant water line to effluent building.
- Contractor completed setting up the SCADA computer in the Operations Building.
- Contractor completed rebar installation for Aeration Basin North Tank center wall.
- Contractor completed installation of the RAS line on the north side of the North Aeration Basin.
- Contractor began installation of fiberglass grating in the Aeration Basin Channel.

KEY WORK ELEMENTS

- Concrete Pour for North Tank Center Wall
- Started Demolition of Old Clarifier Launder Walls and North Tank Top Wall
- RAS Line Installation at North Tank

CONTACT INFORMATION


Justin Skelly, P.E.
Senior Project Manager
413-567-6310 (x703)
justin.skelly@dpcengineering.com

WORK ANTICIPATED DURING THE WEEK OF AUGUST 28, 2023

- Contractor plans to continue forming dividing walls.
- Contractor plans to continue aerator panel wiring.
- Contractor plans to continue miscellaneous site grading.
- Contractor plans to work on stormwater modifications.



*Aeration Tank Center Wall
Concrete Pour*

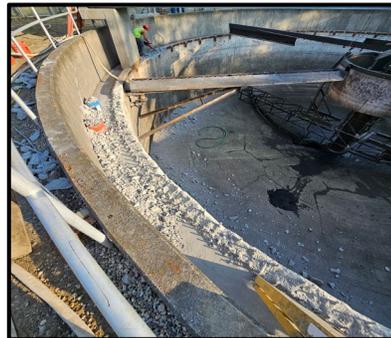

*Demo of Old Clarifier
Launder Walls*



North Tank Top Wall Demo



North Tank Rebar



RAS Line Installation
