

# South Deerfield Wastewater Treatment Facility Phase 1 Upgrades Project

**Weekly Project Update (Issued on August 31, 2023)**  
**Town of Deerfield, MA**



## WORK PERFORMED DURING THE WEEK OF AUGUST 28, 2023

- Contractor completed painting the Secondary Clarifier No. 2 centerwell and installing reinforcement supports.
- Contractor completed demolition of old clarifier launder walls.
- Contractor completed installation of temporary safety railings for the North Aeration Basin.
- Contractor began form installation for North Aeration Basin center wall.
- Contractor started running electrical conduits for new site entrance slide gate and backfilled and compacted trench.
- Contractor completed connection of 8-inch RAS line to the North Aeration Basin.

## KEY WORK ELEMENTS


- Demolition of Old Clarifier Launder Walls
- Building Forms for North Aeration Basin Center Wall
- 8-Inch RAS Line Connection to North Aeration Basin

## CONTACT INFORMATION


Justin Skelly, P.E.  
Senior Project Manager  
413-567-6310 (x703)  
[justin.skelly@dpcengineering.com](mailto:justin.skelly@dpcengineering.com)

## WORK ANTICIPATED DURING THE WEEK OF SEPTEMBER 4, 2023

- Contractor plans to complete concrete pour for North Aeration Basin center wall.
- Contractor plans to continue Secondary Clarifier No. 2 wall modification.
- Contractor plans to install rebar for Effluent Building wall.
- Contractor plans to continue miscellaneous site grading.

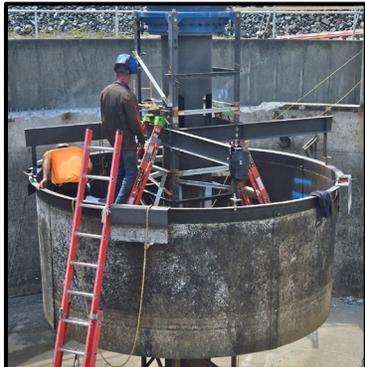


Clarifier Centerwell Painting and Supports

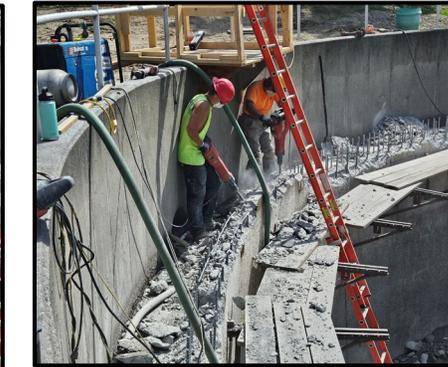

Demo of Old Clarifier Launder Walls



North Tank Safety Railings

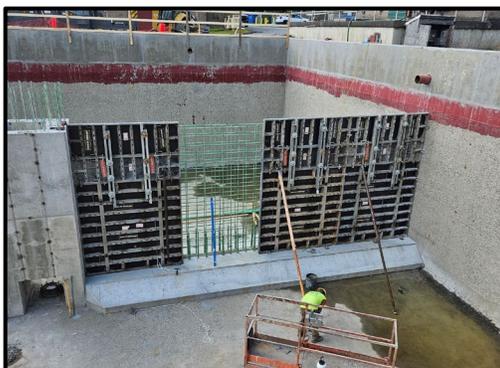

North Tank Center Wall Forms



Electrical Conduit for Front Gate



8-Inch RAS Line Connection
