

# South Deerfield Wastewater Treatment Facility Phase 1 Upgrades Project



**Weekly Project Update (Issued on September 28, 2023)  
Town of Deerfield, MA**

## WORK PERFORMED DURING THE WEEK OF SEPTEMBER 25, 2023

- Contractor continued rebar and form installation for North Aeration Basin distribution channel wall.
- Contractor continued rebar installation for Secondary Clarifier No. 2 wall extension.
- Contractor completed demolition of discharge pipe section at the north wall of Secondary Clarifier No. 2 and prepped for new tie-in.
- Contractor continued installation of PVC pipe that will tie into sump pump in the Chlorine Building basement.
- Contractor completed installation of flashing on Operations Building roof.
- Contractor began saw-cutting the south wall of the North Aeration Basin for demolition.
- Contractor began paving the site driveway with base and top coat.

## KEY WORK ELEMENTS


- Distribution Channel Wall Forms and Rebar
- Secondary Clarifier Wall Extension Rebar Installation
- Operations Building Roof Flashing
- Paving Site Driveway

## CONTACT INFORMATION

Justin Skelly, P.E.  
Senior Project Manager  
413-567-6310 (x703)  
[justin.skelly@dpcengineering.com](mailto:justin.skelly@dpcengineering.com)

## WORK ANTICIPATED DURING THE WEEK OF OCTOBER 2, 2023

- Contractor plans to finish forming North Aeration Basin distribution channel wall and complete a concrete pour for the wall.
- Contractor plans to install the site fencing.
- Contractor plans to begin working on the Effluent Building wall and dividing wall footings.
- Contractor plans to continue walkway conduit installation.

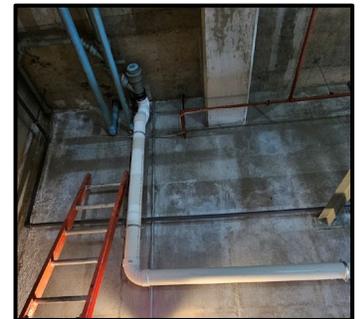

*Distribution Channel Rebar*

*Clarifier Wall Extension Rebar*

*Discharge Pipe Demo*

*Chlorine Building PVC Pipe*



*Operations Building Roof Flashing*

*Saw-Cutting Aeration Basin South Wall*

*Site Paving*
