

South Deerfield Wastewater Treatment Facility Phase 1 Upgrades Project



**Weekly Project Update (Issued on October 5, 2023)
Town of Deerfield, MA**

WORK PERFORMED DURING THE WEEK OF OCTOBER 2, 2023

- Contractor completed wiring of electric heaters in the Headworks Building.
- Contractor completed form work and concrete pour for the North Aeration Basin distribution channel.
- Contractor continued rebar installation for the Secondary Clarifier No. 2 wall extension.
- Contractor completed new drain installation in the basement sump pit in the Effluent Building.
- Contractor completed backfilling and compacting near Secondary Clarifier No. 2 due to rain washout.
- Contractor completed connection of potable water line in the Headworks Building.
- Contractor began installation of Secondary Clarifier No. 2 launder wall forms.

KEY WORK ELEMENTS

- North Basin Distribution Channel Concrete Pour
- Secondary Clarifier Wall Extension Rebar
- Drain Installation in Effluent Building
- Secondary Clarifier Launder Wall Form Installation

CONTACT INFORMATION


Justin Skelly, P.E.
Senior Project Manager
413-567-6310 (x703)
justin.skelly@dpcengineering.com

WORK ANTICIPATED DURING THE WEEK OF OCTOBER 9, 2023


- Contractor plans to continue Secondary Clarifier No. 2 launder wall extension.
- Contractor plans to pour Aeration Basin wall footings and pour clarifier wall.
- Contractor plans to complete installation of site fencing and gate.
- Contractor plans to continue Aeration Basin south tank panel wiring.



Wiring Electric Heaters

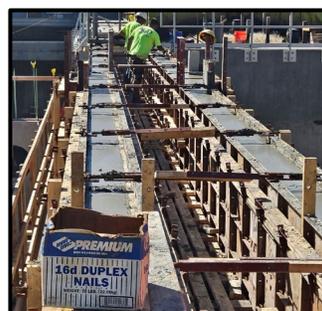

Distribution Channel
Concrete Pour

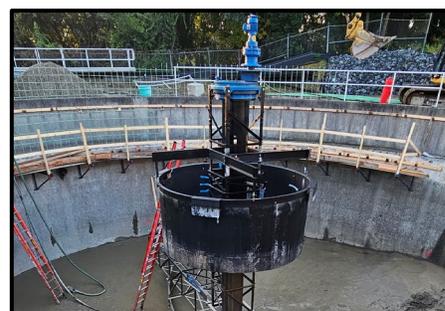


Secondary Clarifier Wall Extension



Effluent Building Drain
Installation



Backfilling Secondary Clarifier No. 2

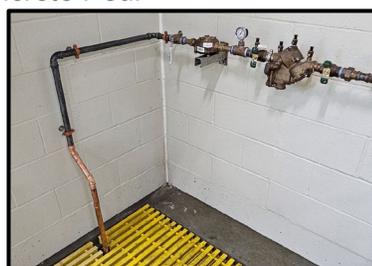

Potable Water Line Connection



Clarifier No. 2 Launder Wall Forms
