

# South Deerfield Wastewater Treatment Facility Phase 1 Upgrades Project



**Weekly Project Update (Issued on October 19, 2023)  
Town of Deerfield, MA**

## WORK PERFORMED DURING THE WEEK OF OCTOBER 16, 2023

- Contractor completed new exterior fence and gate installation.
- Contractor completed removal of hardware and forms on east side launder wall.
- Contractor continued to install forms and rebar for secondary clarifier launder wall extension.
- Contractor started installation of monitor panel in process building for dissolved oxygen.
- Contractor continued wet saw cutting and demolition of center wall between north and south aeration basins.
- Started installation and grouting of slide gates of north tanks and center wall.

## KEY WORK ELEMENTS

- Completed New Exterior Fence and Gate Installation
- East side Launder Wall Form Removal
- Monitor Panel for Dissolved Oxygen Installation
- North and South Aeration Basin Center Wall Demolition

## WORK ANTICIPATED DURING THE WEEK OF OCTOBER 23, 2023


- Contractor plans to form effluent building wall.
- Contractor plans to pour launder wall.
- Contractor plans to form first half of clarifier launder wall.
- Contractor plans to continue aerator conduit and wire.
- Contractor plans to continue SCADA integration and south tank panel startup.

## CONTACT INFORMATION

Justin Skelly, P.E.  
Senior Project Manager  
413-567-6310 (x703)  
[justin.skelly@dpcengineering.com](mailto:justin.skelly@dpcengineering.com)




*New Exterior Fence  
Post Installation*



*East Side Launder Wall  
Form Removal*



*Secondary Clarifier Launder Wall  
Extension Form and Rebar Installation*

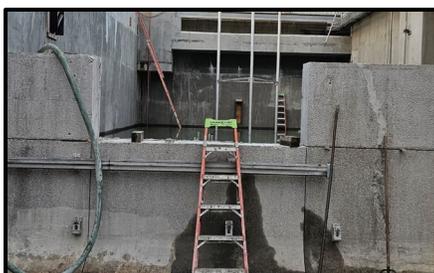

*Aeration Center Wall  
Demo*



*Monitor Panel for  
Dissolved Oxygen*



*Slide Gates of North  
Tanks and Center Walls*

