

South Deerfield Wastewater Treatment Facility Phase 1 Upgrades Project

*Weekly Project Update (Issued on December 1, 2023)
Town of Deerfield, MA*



WORK PERFORMED DURING THE WEEK OF NOVEMBER 27, 2023

- Contractor completed installation of 24-inch ductile iron effluent line to secondary clarifier.
- Contractor continued installation of handrails on north aeration basin distribution channel.
- Contractor continued rebar work for north/south aeration tank dividing wall.
- Contractor completed installation of mooring posts, aerators and mixers in the north tank.
- Contractor completed installation of weir plates on slide gates in north aeration distribution channel.

WORK ANTICIPATED DURING THE WEEK OF DECEMBER 4, 2023

- Contractor plans to continue rebar and formwork on north tank wall.
- Contractor plans to complete installation of secondary clarifier mechanisms for testing.
- Contractor plans to install 36-inch spool pieces and slide gates in the north aeration tank.
- Contractor plans to continue installation of electrical conduits for north aeration tank aerators and mixers.

KEY WORK ELEMENTS

- 24-Inch Ductile Iron Effluent Line Installation
- Rebar Work for North/South Aeration Tank Dividing Wall Installation
- Mooring Post, Aerator and Mixer Installation

CONTACT INFORMATION


Justin Skelly, P.E.
Senior Project Manager
413-567-6310 (x703)
justin.skelly@dpcengineering.com



24-Inch Ductile Iron Effluent Line Installation



Handrail Installation

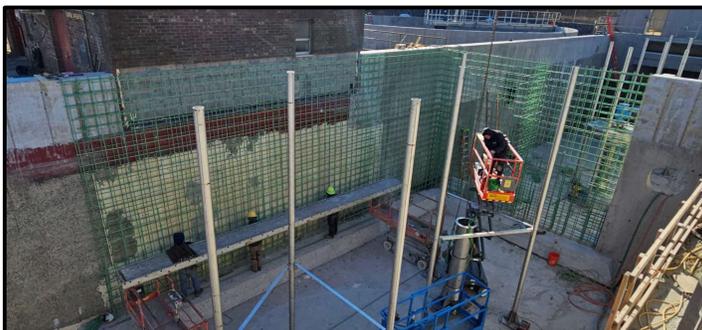

*North/South Aeration Tank
Dividing Wall Rebar Installation*



*Aerator and Mixer
Installation*



Weir Plate Installation
