

South Deerfield Wastewater Treatment Facility Phase 1 Upgrades Project



**Weekly Project Update (Issued on December 7, 2023)
Town of Deerfield, MA**

WORK PERFORMED DURING THE WEEK OF DECEMBER 4, 2023

- Contractor completed rebar work and started installation of wall forms for north/south aeration tank dividing wall.
- Contractor continued running electrical conduits and junction boxes to north aeration basin for mixer/aerator power.
- Contractor completed installation of two 36-inch spool pieces for slide gate in north/west aeration basin.
- Contractor started filling secondary clarifier for startup and testing.
- Contractor completed installation of light pole for north aeration tank.

KEY WORK ELEMENTS

- Installation of Electrical Conduit for North Aeration Basin Mixer/Aerator
- Installation of Forms and Rebar for North/South Aeration Tank Dividing Wall
- Installation of 36-Inch Spool Piece for Slide Gate in North/West Aeration Basin

WORK ANTICIPATED DURING THE WEEK OF DECEMBER 11, 2023

- Contractor plans to pour concrete for the north/south aeration tank dividing wall.
- Contractor plans to startup and test secondary clarifier and check motor operations.
- Contractor plans to continue installation of electrical conduits for north aeration tank aerators and mixers.

CONTACT INFORMATION


Justin Skelly, P.E.
Senior Project Manager
413-567-6310 (x703)
justin.skelly@dpcengineering.com



North/South Aeration Tank Wall Form and Rebar Installation



*North Aeration Basin
Electrical Conduit Installation*

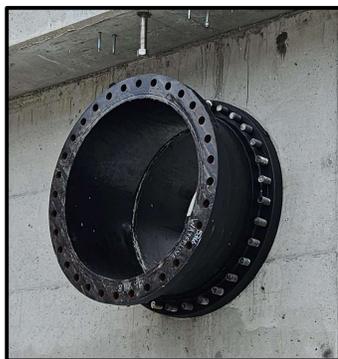

*36-Inch Spool Piece for
Slide Gate Installation*



*Secondary Clarifier
Startup and Testing*



*Light Pole
Installation*
