

# South Deerfield Wastewater Treatment Facility Phase 1 Upgrades Project



**Weekly Project Update (Issued on March 11, 2024)  
Town of Deerfield, MA**

## **WORK PERFORMED BY CONTRACTOR DURING THE WEEKS OF FEBRUARY 26, 2024 & MARCH 4, 2024**

- Installed forms and rebar for north tank concrete stairs.
- Poured and removed forms for north tank concrete stairs.
- Installed mixer for south aeration basin tank A.
- Installed handrails for north/south aeration basin tanks A and B.

## **KEY WORK ELEMENTS**

- Installed Forms and Rebar and Poured North Tank Concrete Stairs Slab
- Installed Mixer for South Aeration Basin Tank A

## **WORK ANTICIPATED BY CONTRACTOR DURING THE WEEKS OF MARCH 11 & 18, 2024**


- Plans to continue installing forms for stair supports.
- Plans to pour concrete for stair supports.
- Plans to continue installation of hand rails.
- Plans to start loaming around Clarifier No. 1 and Operations Building.

## **CONTACT INFORMATION**

Justin Skelly, P.E.  
Senior Project Manager  
413-567-6310 (x703)  
[justin.skelly@dpcengineering.com](mailto:justin.skelly@dpcengineering.com)



*Form and Rebar Installation and Concrete Pour  
for North Tank Concrete Stairs*

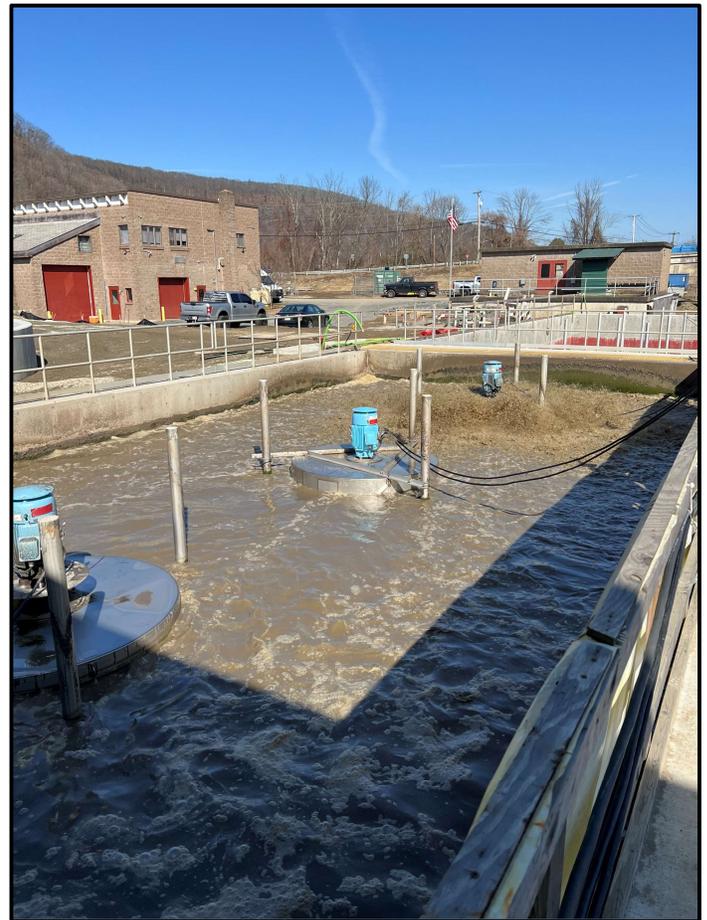

*Mixer Installation for South Aeration Basin Tank A*
