

South Deerfield Wastewater Treatment Facility Phase 1 Upgrades Project

*Project Update (Issued on May 6, 2024)
Town of Deerfield, MA*



WORK PERFORMED BY CONTRACTOR DURING THE WEEKS OF APRIL 22, 2024 AND APRIL 29, 2024

- Completed installation of 36-inch slide gates between Aeration Tanks A & C.
- Finished concrete pour and form removal for the North Aeration Tank concrete stairs and installed handrails.
- Continued running electrical conduit for modular plugs associated with Mixer and Aeration tanks.
- Final paving for sidewalks, driveways, and in-between tanks.
- Final site landscaping including hydroseeding designated areas of property.

KEY WORK ELEMENTS

- North Tank Stairs Form Removal and Handrail Installation
- Conduit Installation for Mixer and Aeration Tanks
- Continued Paving Areas Around Site

CONTACT INFORMATION


Justin Skelly, P.E.
Senior Project Manager
413-567-6310 (x703)
justin.skelly@dpcengineering.com

WORK ANTICIPATED BY CONTRACTOR DURING THE WEEKS OF MAY 6, 2024 & MAY 13, 2024

- Plans to finalize outstanding punchlist items.
- Plans to finish installation of Aerator/Mixer on Tank C and Clarifier 2 Motor
- After completing the punchlist items, proceed with demobilizing equipment off-site.



Hydroseeding

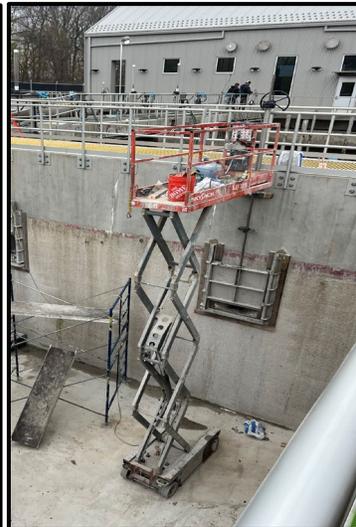

Slide Gates Installation



Paving for Parking Lots and Sidewalks

